

CONFIDENTIAL — CLIENT DOCUMENT

Project Master Overview

Alsultania Travel CRM & Management System

PREPARED FOR

Alsultania Travel and Tourism Co. L.L.C
Dubai, United Arab Emirates

PREPARED BY

AnyMatch Technologies Private Limited

VERSION

1.0

LAST UPDATED

11 June 2026

CURRENT PHASE

Phase 0 — Blueprint (pending approval)

This document is confidential and prepared exclusively for Alsultania Travel and Tourism Co. L.L.C and AnyMatch Technologies Private Limited.

Table of Contents

- 1. Quick Access
 - 2. What This Project Is
 - 3. Documentation Index
 - 4. Interactive Prototype
 - 5. Figma & Design Assets
 - 6. Delivery Phases & Modules
 - 7. Screen Inventory
 - 8. Technology Stack
 - 9. Change Management
 - 10. Client Dependencies
-

1. Quick Access

Resource	Link / Path
Documentation index	README.md
This master file	PROJECT_MASTER.md
Requirements (authoritative)	requirements/SRS.md v1.0
Phase 0 acceptance form	requirements/PHASE_0_ACCEPTANCE.md
Lead lifecycle (client summary)	client/LEAD_LIFECYCLE.md
Software design (SDD)	design/SOFTWARE_DESIGN_DOCUMENT.md
Database schema	design/DATABASE_SCHEMA.md
Diagrams (Mermaid)	diagrams/
Blueprint status summary	blueprint/BUEPRINT_DELIVERABLE.md
Lead creation deep-dive	requirements/SRS.md Appendix C
Required third-party services	requirements/SRS.md Appendix D
Development guide	development/DEVELOPMENT_GUIDE.md
Figma import instructions	blueprint/FIGMA_IMPORT_GUIDE.md
Prototype cover page	../prototype/cover.html
Screen QA index	../prototype/screens-index.html
Figma design file	design-travel_crm
FigJam ERD + flows	FigJam board
Import manifest	../the blueprint import manifest
PNG screenshots	../figma-export/screenshots/

2. What This Project Is

A **full-stack travel agency CRM** that unifies:

- Lead capture, assignment, and pipeline management — including **public website inquiry** (phone OTP → required fields → auto-assign to next available agent)
- Customer profiles and booking workflows
- Financial accounting, invoicing, and expense controls
- Staff performance and HR metrics
- WhatsApp automation and multi-channel notifications
- Reporting, analytics, and multi-branch scalability

Phase 0 (current) delivers the approved blueprint: screen flows, data model, component library, and requirements specification. **Development (Phases 1–3)** begins only after client approval of the Figma blueprint.

Phase	Focus	Screens	Cost (PKR)
0	Blueprint — flows, ERD, components	4 overview + planning	80,000
1	Core CRM, leads, customers, bookings	01–12 (+ 05a–05d)	220,000
2	Accounting, expenses, HR	13–23	200,000
3	Reports, automation, multi-branch	24–33	150,000
	Total	37 app screens	650,000

```

travel_crm/
├── README.md                ← Root pointer to docs/
├── docs/                    ← All software development documentation
│   ├── PROJECT_MASTER.md    ← YOU ARE HERE – project entry point
│   ├── README.md            ← Documentation index
│   ├── requirements/
│   │   ├── SRS.md           ← Authoritative spec (Appendices A-D incl. lead creation & third-pa
│   │   └── PHASE_0_ACCEPTANCE.md ← Client signing form for Phase 0 blueprint approval
│   ├── client/
│   │   └── LEAD_LIFECYCLE.md ← Client-facing lead pipeline summary
│   ├── blueprint/
│   │   ├── BLUEPRINT_DELIVERABLE.md
│   │   └── FIGMA_IMPORT_GUIDE.md
│   ├── design/
│   │   ├── SOFTWARE_DESIGN_DOCUMENT.md
│   │   ├── DATABASE_SCHEMA.md
│   │   └── API_INTEGRATIONS.md
│   ├── development/
│   │   ├── DEVELOPMENT_GUIDE.md
│   │   ├── TESTING_STRATEGY.md
│   │   └── DEPLOYMENT_CHECKLIST.md
│   └── diagrams/            ← Mermaid source files (.mmd)
│       ├── erd.mmd
│       ├── system-architecture.mmd
│       └── ... (see diagrams/README.md)
├── the blueprint import manifest ← Screen → URL → Figma page mapping
├── prototype/               ← Interactive HTML blueprint (40 files)
│   ├── cover.html           ← Phase 0 cover & index
│   ├── index.html           ← Master screen flow diagram
│   ├── components.html      ← UI component library
│   ├── data-architecture.html ← ERD view
│   ├── screens-index.html   ← QA table of all screens
│   ├── styles.css           ← Shared prototype styles
│   ├── nav.js               ← Shared navigation
│   ├── lead-form-shared.js   ← Shared lead form logic
│   ├── *.html               ← 33 application screen prototypes
│   └── *.js                 ← Screen-specific interactivity
├── figma-export/
│   └── screenshots/         ← Pre-captured PNGs by phase folder
├── figma-scripts/
│   └── 01-create-pages.js    ← Figma MCP page creation script
├── scripts/
│   ├── capture-screenshots.mjs ← Re-capture PNGs via Playwright
│   └── wire-prototype-links.mjs ← Wire inter-screen navigation
└── node_modules/            ← Playwright (screenshot tooling only)


```

4. Documentation Index

Client-facing reference documents (PDF set):

Document	Purpose
Project Master Overview	Project hub, phases, screen inventory, dependencies
Software Requirements Specification (SRS)	Authoritative requirements baseline (Phases 0–3)
Phase 0 Acceptance Form	Blueprint attestation and scope decisions
Lead Lifecycle Summary	Pipeline stages, transitions, and agent actions
Blueprint Deliverable Summary	Phase 0 completion status and screen list
Deployment Checklist	Production go-live steps for client IT
Architecture Diagrams	ERD, flows, lifecycle, and delivery timeline (PDF set)

Document hierarchy

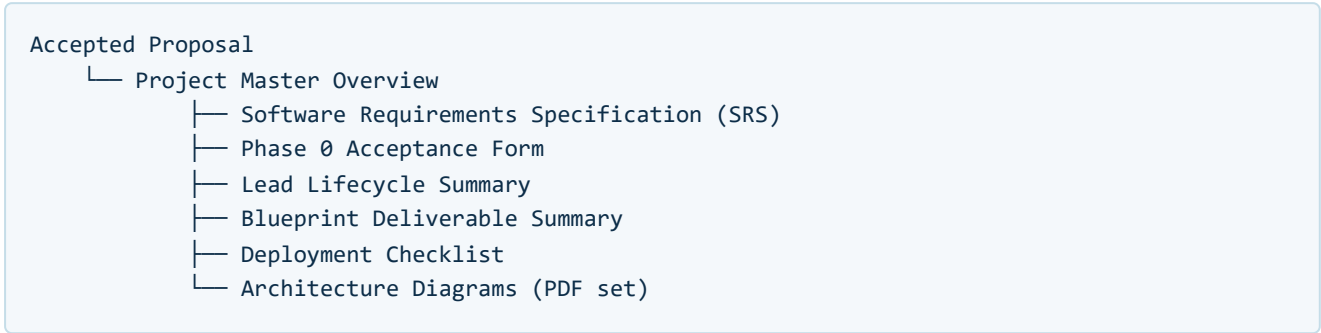

Rule: The SRS is the authoritative requirements document. The HTML prototype and FigJam board are visual references for blueprint review.

5. Interactive Prototype

The **Interactive Prototype (40 screens)** folder is a **clickable HTML blueprint** — not production code. It demonstrates layout, navigation, fields, and flows at 1440px width.

Overview frames (Phase 0)

Frame	File	Description
Cover & Index	<code>cover.html</code>	Project summary, phase costs, quick links
Master Screen Flow	<code>index.html</code>	Visual map of all 37 screens and connections
Component Library	<code>components.html</code>	Buttons, badges, cards, tables, form fields
Data Architecture	<code>data-architecture.html</code>	ERD diagram (links to FigJam)
Screen Index (QA)	<code>screens-index.html</code>	Sortable table of every frame

Shared assets

File	Role
<code>styles.css</code>	Design tokens, layout, components
<code>nav.js</code>	Top navigation bar across screens
<code>lead-form-shared.js</code>	Dynamic lead type fields, subject generation
<code>leads-create.js</code>	Staff create lead interactivity
<code>inquiry-otp.js</code> / <code>inquiry-create.js</code>	Public website OTP verification + inquiry form submit

Public website inquiry flow (Phase 1)

Customers submit leads on the agency **public website** (`/inquiry`) without CRM login. Full spec: `requirements/SRS.md` [Appendix C §1a](#).

Step	Prototype	What happens
1	<code>inquiry-otp.html</code> (05b)	Customer enters mobile number; system sends 6-digit SMS OTP
2	<code>inquiry-otp.html</code> (05b)	Customer verifies OTP; verified phone stored in session
3	<code>inquiry-create.html</code> (05c)	Customer completes required fields (name, service type, type-specific fields, dates & travelers)
4	System (AUTO-02)	Lead saved with <code>lead_via</code> = Website; auto-assigned to next available active agent
5	<code>inquiry-success.html</code> (05d)	Customer sees confirmation with reference ID (agent assignment is internal)

Staff Create Lead (`leads-create.html`) uses the same field model but requires CRM login and manual **Lead Handling** (Takeover / Others / Transfer).

Key user journeys (prototype)

Journey	Screens
Staff login → dashboard → new lead	<code>login.html</code> → <code>dashboard.html</code> → <code>leads-create.html</code>
Public website inquiry (no login)	<code>inquiry-otp.html</code> → <code>inquiry-create.html</code> → <code>inquiry-success.html</code>
Lead lifecycle	<code>leads-list.html</code> → <code>lead-detail.html</code> → <code>pipeline.html</code>
WhatsApp capture	<code>whatsapp-inbox.html</code> → <code>leads-create.html</code>

6. Figma & Design Assets

Asset	URL / Path	Status
Figma Design File	design-travel_crm	Ready to import (see guide)
FigJam — ERD + Flows	Board	Complete
PNG Screenshots	figma-export/screenshots/	Complete (37 + overview)
Import manifest	the blueprint import manifest	Maps every screen → Figma page

Figma page structure

Page	Contents
00 – Cover & Index	Cover frame
01 – Master Screen Flow	Flow diagram
02 – Phase 1: Core CRM	Screens 01–12, 05a–05d
03 – Phase 2: Financials & HR	Screens 13–23
04 – Phase 3: Automation & Scale	Screens 24–33
05 – Components	Component library

See `blueprint/FIGMA_IMPORT_GUIDE.md` for import options (html.to.design plugin, PNG drag, or Figma MCP).

7. Delivery Phases & Modules

Phase 1 — Core CRM (Screens 01–12)

Authentication, RBAC, dashboard, advanced lead management (staff create + **public website inquiry with OTP and auto-assignment**), pipeline, WhatsApp inbox, customers, bookings.

Key specs: SRS §4.1 (FR-18*, AUTO-02), SRS [Appendix C §1a](#) (public), [Appendix C §2](#) (staff)

Phase 2 — Financials & HR (Screens 13–23)

Accounting dashboard, revenue, invoices, payments, financial reports, expenses, approvals, staff performance, attendance, cost centres.

Key specs: SRS §4.2

Phase 3 — Automation & Scale (Screens 24–33)

Reports hub, custom report builder, notifications, communication templates, channel settings, automation rules, workflow triggers, multi-branch, consolidated view, system settings.

Key specs: SRS §4.3, §5 (automation)

User roles

Role	Primary modules
Administrator	All modules, settings, automation, branches
Sales Manager	Leads, team, reports, approvals
Travel Agent	Leads, customers, bookings, WhatsApp
Finance User	Accounting, invoices, expenses (Phase 2)
HR/Manager	Performance, attendance (Phase 2)

Full RBAC matrix: SRS §3.1

8. Screen Inventory

Phase 0 — Overview (4 frames)

#	Screen	Prototype File
—	Cover & Index	Interactive Prototype (cover page)
—	Master Screen Flow	Interactive Prototype
—	Component Library	Component Blueprint Library
—	Data Architecture ERD	prototype/data-architecture.html

Phase 1 — Core CRM (16 screens)

#	Screen	Prototype File
01	Login	prototype/login.html
02	User Management	prototype/user-management.html
03	Roles & Permissions	prototype/roles-permissions.html
04	Dashboard	prototype/dashboard.html
05	Leads List	prototype/leads-list.html
05a	Create Lead (Staff)	prototype/leads-create.html
05b	Verify Phone (OTP) — Public Website	prototype/inquiry-otp.html
05c	Public Inquiry Form — Required Fields	prototype/inquiry-create.html
05d	Inquiry Submitted — Confirmation	prototype/inquiry-success.html
06	Lead Pipeline	prototype/pipeline.html
07	Lead Detail	prototype/lead-detail.html
08	WhatsApp Inbox	prototype/whatsapp-inbox.html
09	Customer List (full mockup)	prototype/customer-list.html
10	Customer Profile (full mockup)	prototype/customer-profile.html
11	Booking List	prototype/booking-list.html
11a	New Booking	prototype/booking-create.html
12	Booking Detail	prototype/booking-detail.html

Phase 2 — Financials & HR (11 screens)

Accounts top-nav dropdown groups: **Customers** · **Receivables** (Finance Dashboard, Payment Queue, Invoices, Revenue Adjustments) · **Payables** (Expenses, Log Expense, Expense Approvals, Cost Centres) · **Analysis** (Financial Reports). See [the approved blueprint navigation](#) and SRS §4.2.1a.

#	Screen	Prototype File
13	Finance Dashboard	prototype/accounting-dashboard.html
14	Revenue Adjustments	prototype/revenue-recording.html
15	Invoice List	prototype/invoice-list.html
16	Payment Queue	prototype/payment-tracking.html
17	Financial Reports (full mockup)	prototype/financial-reports.html
18	Expense List (full mockup)	prototype/expense-list.html
19	Log Expense (full mockup)	prototype/log-expense.html
20	Expense Approvals (full mockup)	prototype/expense-approvals.html
21	Staff Performance	prototype/staff-performance.html
22	Attendance & HR	prototype/attendance-hr.html
23	Cost Centres (full mockup)	prototype/cost-centres.html

Phase 3 — Automation & Scale (10 screens)

Reports top-nav dropdown groups: **Reports Hub** · **Report Builder** · **Performance** (Staff Performance, Attendance & HR) · **Management** (Consolidated View). Financial Reports remains under Accounts → Analysis. See [the approved blueprint navigation](#) and SRS §4.3.1a.

#	Screen	Prototype File
24	Reports Hub	prototype/reports-hub.html
25	Report Builder	prototype/report-builder.html
26	Notifications	prototype/notifications-center.html
27	Templates	prototype/communication-templates.html
28	Channel Settings	prototype/channel-settings.html
29	Automation Rules	prototype/automation-rules.html
30	Workflow Triggers	prototype/workflow-triggers.html
31	Multi-Branch	prototype/multi-branch.html
32	Consolidated View	prototype/consolidated-view.html
33	System Settings	prototype/system-settings.html

Full requirement IDs per screen: SRS §4 and Appendix A.

9. Technology Stack

Layer	Technology
Backend (planned)	Laravel (PHP 8.x)
Database (planned)	MySQL 8.x
Frontend (planned)	Laravel Blade, component-based UI
Messaging	WhatsApp Business API (client-provisioned) — see SRS Appendix D
Public inquiry OTP	SMS gateway (client-provisioned) — see SRS Appendix D
Email	SMTP (client-provisioned) — see SRS Appendix D
Blueprint prototype	Static HTML/CSS/JS
Screenshot tooling	Playwright (Node.js)
Design	Figma + FigJam

Production application code is **not yet in this repository** — current contents are Phase 0 blueprint artifacts only.

Prototype server

```
cd C:/laragon/www/travel_crm/prototype && php -S 127.0.0.1:8765
```

Re-capture Figma PNG screenshots

Scripts auto-start the PHP server from **Interactive Prototype (40 screens)** (required — starting from repo root causes 404 screenshots):

```
cd C:/laragon/www/travel_crm
node scripts/capture-screenshots.mjs
node scripts/capture-lead-creation-screenshots.mjs
```

Output: `figma-export/screenshots/` and `lead creation/`

If you start the server manually, **must** use:

```
cd C:/laragon/www/travel_crm/prototype && php -S 127.0.0.1:8765
```


Wire prototype navigation links

```
cd C:/laragon/www/travel_crm  
node scripts/wire-prototype-links.mjs
```

Figma MCP import (when Pro plan available)

1. Run `figma-scripts/01-create-pages.js` via Figma MCP `use_figma`
 2. Run `generate_figma_design` for each URL in `the blueprint import manifest`
-

11. Change Management

After Phase 0 blueprint approval, the accepted SRS and Figma blueprint are the **locked baseline** for development.

- Post-approval changes to screens, fields, flows, or scope require **written agreement** between Client and Vendor
- Commercial terms and pricing remain governed by the accepted proposal
- Client dependencies (server, WhatsApp, SMS, SMTP) must be ready per the timelines in the SRS

For questions about scope or acceptance criteria, refer to the SRS §9 (Phase-wise Delivery & Acceptance).

Client Dependencies (Before Phase 1 Development)

Full detail, credentials checklist, and go-live requirements: [requirements/SRS.md](#) **Appendix D** and **Deployment Checklist**

Dependency	Required before
Figma blueprint approval	Phase 1 start
Server provisioning (PHP, MySQL, HTTPS)	Phase 1 start
WhatsApp Business API access	Phase 1 go-live
SMS gateway for public inquiry OTP	Phase 1 go-live
Email SMTP (transactional)	Phase 1 go-live
Designated project email contacts	Project commencement

Maintained as part of the Alsultania Travel CRM Phase 0 blueprint. For questions about scope or acceptance criteria, refer to [requirements/SRS.md](#) §9.
